



SAPIENZA
UNIVERSITÀ DI ROMA

Napoli Liber/Azione

DIGITAL PRESERVATION OF HISTORICAL MEMORY

TEAM 400

Mirco Soriano 2205397

Hanna Vollmo Oster 2118620

Bogdan Andrei Tutuianu 2217481

Jonah Sjolín 2286061



AGENDA

-  **01** | **Project Description**
-  **02** | **Project Scope**
-  **03** | **Project Structure**
-  **04** | **Roles and Responsibilities**
-  **05** | **Main Criticalities**
-  **06** | **Project Critical Evaluation**
-  **07** | **Conclusion**



NAPOLI LIBER/AZIONE

DIGITAL PRESERVATION OF HISTORICAL MEMORY

A digital platform to preserve and enhance the historical memory of the Four Days of Naples through multimedia storytelling, digital archive and accessible technologies.



PROJECT GOALS



PRESERVE HISTORICAL MEMORY

Safeguard and valorize the memory of the Four Days of Naples for future generations.



PROMOTE ACCESSIBILITY

Ensure an inclusive and accessible experience for all users.



ENHANCE USER ENGAGEMENT

Offer interactive storytelling and multimedia content to engage citizens.



CREATE LONG-TERM DIGITAL VALUE

Generate sustainable cultural value through digital innovation.




NAPOLI LIBER/AZIONE

DIGITAL PRESERVATION OF HISTORICAL MEMORY

WHO	WHY	WHAT	WHERE	WHEN
 Graf S.R.L. & Partenope Project Lab   	  Preserve and disseminate the historical memory  Promote cultural awareness and social engagement  Use digital innovation to safeguard our heritage 	 Development of a multimedia digital platform with storytelling, digital archive and accessibility features   MULTIMEDIA STORYTELLING  DIGITAL ARCHIVE  ACCESSIBILITY  INTERACTIVE EXPERIENCE	 Web-based digital environment accessible online 	 Early 2024 





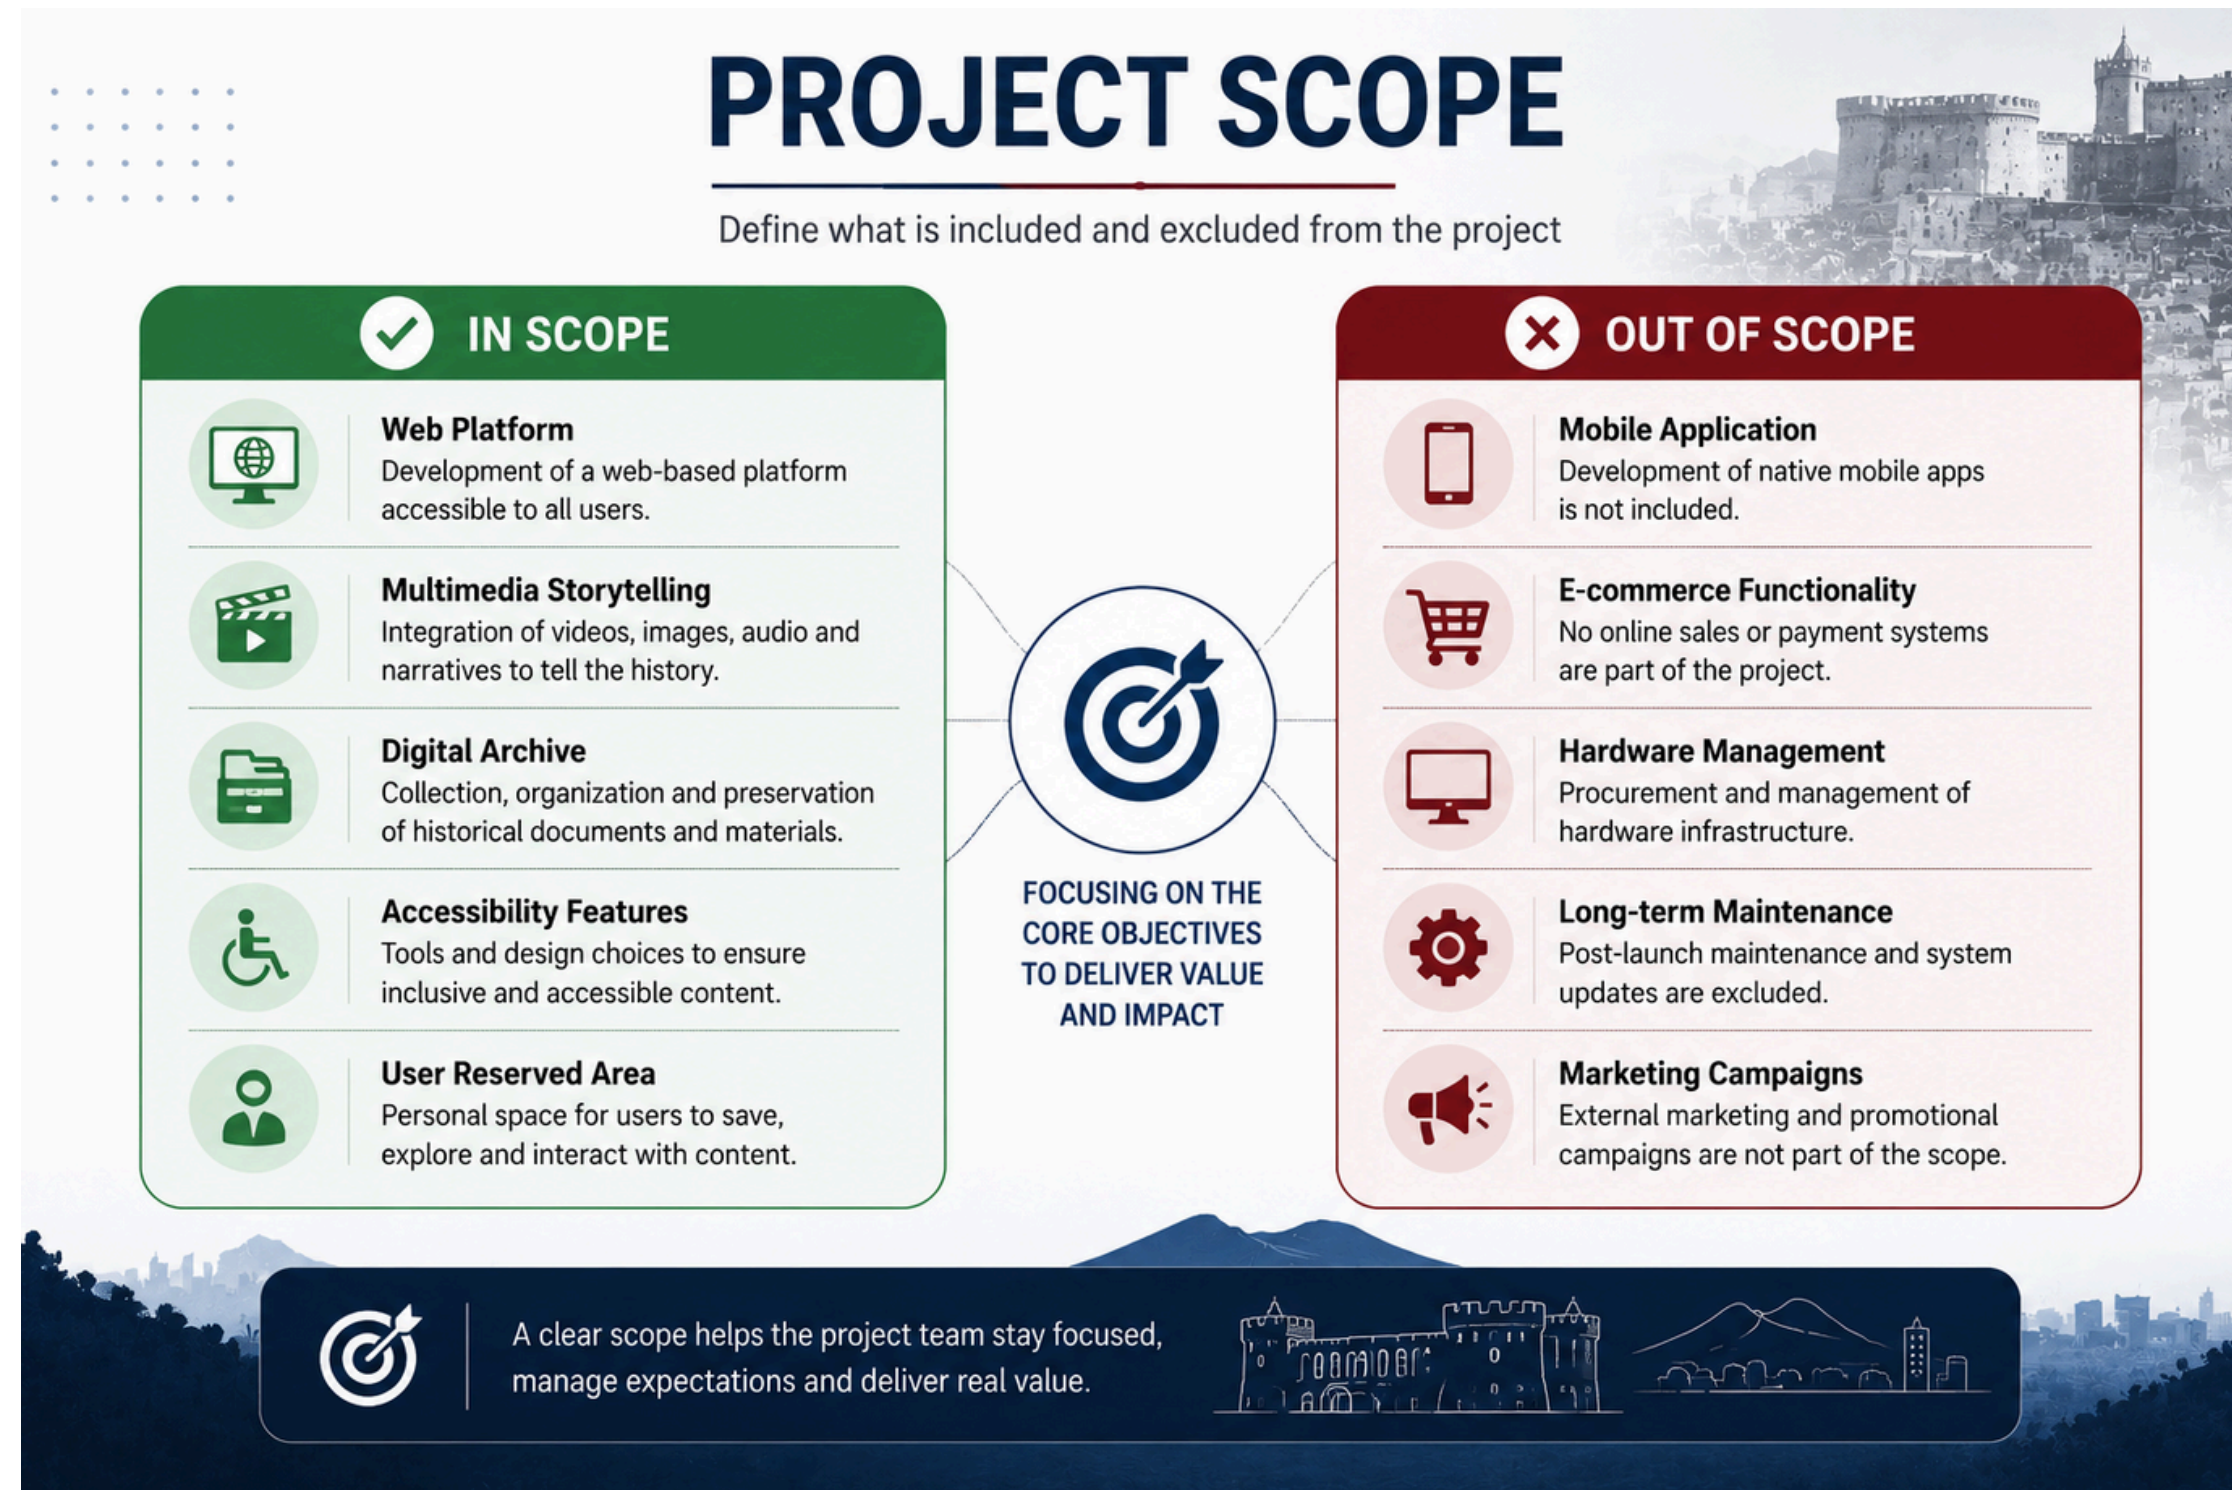




WBS ID	Phase	Work Package	Responsible Role(s)
1.1	Planning and Initiation	Define project requirements	Project Manager
1.2	Planning and Initiation	Prepare resource and financial planning activities	Project Manager
1.3	Planning and Initiation	Define sprint and milestone planning	Project Manager
2.1	Design and Prototyping	Define system architecture and application logic	Senior Developer
2.2	Design and Prototyping	Develop and validate UX/UI prototypes	Project Manager, Development Team
2.3	Design and Prototyping	Collect and organise platform materials	Communication Team, Client, Project Manager
3.1	Core Development and Feature Implementation	Configure database functionalities	Junior Developers, Senior Developer
3.2	Core Development and Feature Implementation	Implement authentication and access functionalities	Junior Developers, Senior Developer
3.3	Core Development and Feature Implementation	Develop advanced search functionality	Junior Developers, Senior Developer
3.4	Core Development and Feature Implementation	Implement subscription functionalities	Junior Developers, Senior Developer
3.5	Core Development and Feature Implementation	Develop streaming and multimedia functionalities	Junior Developers, Senior Developer
3.6	Core Development and Feature Implementation	Define and implement AI-related functionalities	Junior Developers, Senior Developer
3.7	Core Development and Feature Implementation	Integrate external platforms and services	Junior Developers, Senior Developer
4.1	Testing and QA	Conduct functional testing and supervision	Senior Developer, Mid-level Developer
4.2	Testing and QA	Perform beta and advanced testing	Development Team
4.3	Testing and QA	Verify integrations and validate functionalities	Senior Developer, Mid-level Developer
4.4	Testing and QA	Resolve bugs and implement corrections	Development Team
5.1	Documentation, Finalisation and Delivery	Prepare project documentation and reporting	Project Manager, Senior Developer
5.2	Documentation, Finalisation and Delivery	Conduct final review and platform adjustments	Project Manager, Development Team
5.3	Documentation, Finalisation and Delivery	Deliver final platform	Project Manager, Development Team

Work Breakdown Structure

Project Structure

Phase	Approximate duration	Main activities
Planning and Initiation	January – April	Requirements definition, resource planning, financial planning, sprint and milestone planning
Design and Prototyping	January – March	System architecture, UX/UI alignment, prototype development and prototype validation
Core Development and Feature Implementation	March/April – July	Database configuration, implementation of platform functionalities, external integrations, AI-related functionalities
Testing and Quality Assurance	April – July	Functional testing, beta testing, advanced testing, supervision, validation of implemented features
Documentation and Finalisation	May – July	Reporting, technical and business documentation, final review, content production and platform adjustments

Identified Phases of The Project

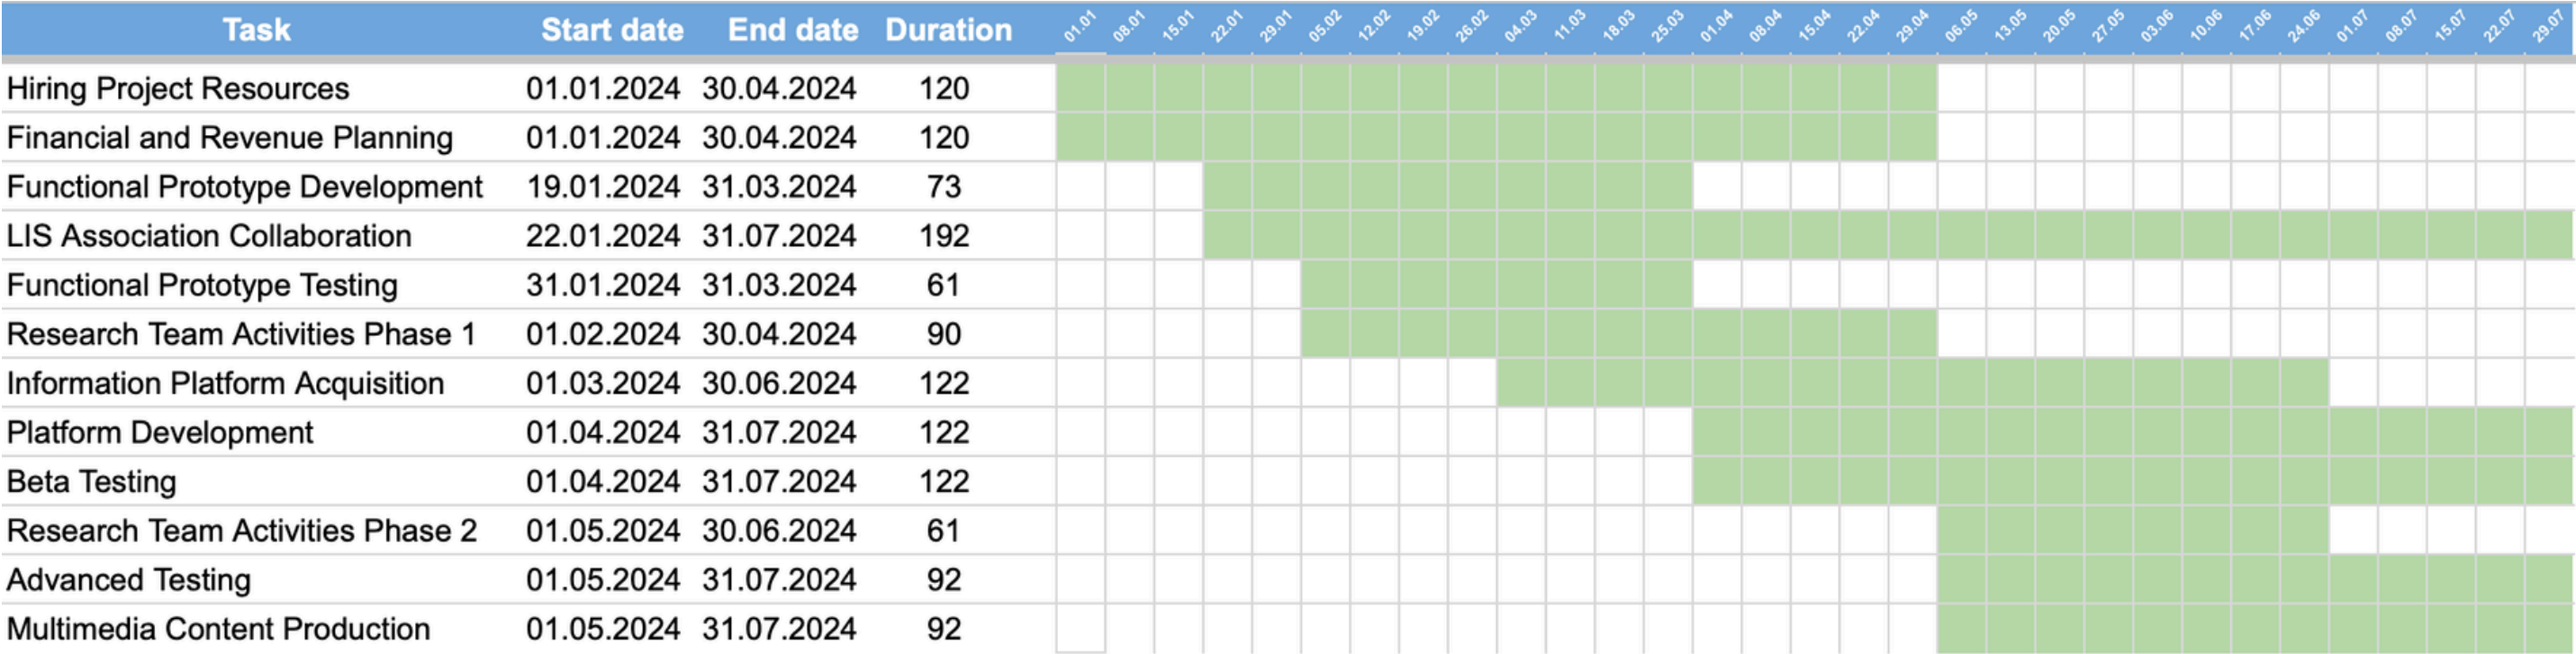

Gantt Chart



Roles and Responsibilities

Role	Main responsibilities
Project Managers	Planning, coordination, stakeholder communication, timeline updates, reporting, documentation, and alignment between technical and business perspectives
Senior Developer	Selected technical development tasks, architecture-related contributions, technology selection, application logic, and externally delivered components
Mid-level Developer	Supervision, validation, quality control, integration support
Junior Developers	Implementation of platform functionalities, technical tasks, and development of core system components

Project Roles and Responsibilities

Project phase	Project Manager	Senior Developer	Mid-level Developer	Junior Developers	Communication Team	Client
Planning and Initiation	A/R	C	I	I	I	C
Design and Prototyping	A	R	C	C	C	C
Core Development and Feature Implementation	A	C	C	R	I	I
Testing and Quality Assurance	A	C	R	R	I	C
Documentation and Finalisation	A/R	C	C	R	I	C
Stakeholder Communication	A/R	I	I	I	C	C
Funding and Reporting Compliance	A/R	I	I	I	I	C

Reconstructed RACI matrix



Effort Based Planning

Resource category	Total hours	Hourly rate	Total cost
Development resource	384	€35.00	€13,440
Development / supervision resource	144	€25.00	€3,600
Junior development resource	360	€21.25	€7,650
Junior development resource	336	€21.25	€7,140
Junior development resource	312	€21.25	€6,630
Project management resource	256	€35.00	€8,960
Project management resource	272	€35.00	€9,520
Total	2,064		€56,940

Cost Overview



Main Criticalities & Particularities

Four dimensions that set this project apart

1 Scope & Contract Misalignment

The project charter and technical annex describe a scope inconsistent with the actual delivered project, creating ambiguity in acceptance criteria and IP rights.

2 Weak Early-Stage Scope Definition

First SAL (Jan 2024) shows large number of unresolved questions on timelines, features, and collaborations.

3 Complex Multi-Stakeholder Structure

Client, developer, PM firm, LIS associations, researchers, and funding body; each with different timelines and accountability levels.

4 External Senior Developer Failure

Outsourced components were delayed and below standard, triggering crashing and fast-tracking, and leaving only €60 of the €57,000 budget.



1 Scope & Contract Misalignment

Original technical quote (Partenope Project Lab, April 2023) describes a scope that diverges from the actual delivered project.

The actual delivered project is a historical/cultural archive preserving the memory of the Quattro Giornate di Napoli.

Risk

Divergence between contractual scope and actual delivery scope creates ambiguity in acceptance criteria, intellectual property rights, and future change requests.

Key PM lesson:

The Project Charter and technical annex must unambiguously describe the actual project, not a generic template.

Main Criticalities & Particularities

2 Weak Early-Stage Scope Definition

At the first SAL (22 Jan 2024), these questions remained open:

- 1 Content creation timeline not defined
- 2 Collaboration structure for researchers (n=4) unclear
- 3 Creative team selection (artists, writers) not started
- 4 15-artist team for installation: TBD
- 5 Filmmakers/reporters for 10 videos: TBD
- 6 Open Call to Naples timeline undefined
- 7 Maschio Angioino exhibition timeline undefined
- 8 QR code placement sites not decided
- 9 Telegram community setup not defined
- 10 AR feature: concept only, no plan

Main Criticalities & Particularities

3 Complex Multi-Stakeholder & Multi-Supplier Structure

Graf SRL	Partenope Project Lab	Gruppo ACTA	LIS Assoc.	Researchers (n=4)
Client	Developer	PM Firm	Accessibility	Historical

Challenge: coordinating 5+ distinct actor groups across cultural, technical, and institutional domains – each with different timelines, expectations, and accountability levels.

4 External Senior Developer Failure

The Problem

- External developer hired to increase capacity while internal team managed concurrent projects.
- Delivered components were both delayed and below technical standards.
- Internal team absorbed unplanned correction, adaptation, and integration work.
- In our analysis, this dependency was classified as high likelihood/high impact; in practice, mitigation relied only on supervision, with no formal acceptance criteria or quality gates for outsourced deliverables.

Response & Consequences

- **Crashing:** internal developer assigned to work alongside supplier, accelerating correction and integration.
- **Fast-tracking:** unaffected workstreams reorganised to run in parallel to recover lost time.
- **Budget impact:** €56,940 spent of €57,000; only €60 remaining – a near-zero contingency margin.
- **Key lesson:** Formal quality gates and acceptance criteria must be embedded in supplier arrangements, not left to informal supervision.



Project Closure

SCOPE

100% of planned technical features delivered. Includes AI storytelling, multimedia archives, and LIS accessibility tools.

COST

€56,940 spent of €57,000 budget ceiling, with 2,064 Hrs total effort spent. Full compliance with TOCC public funding reporting.

TIME

Final delivery milestone met in July 2024. Project completed within the 7-month contractual limit.

QUALITY

Obtained signed test report from Graf S.R.L. certifying full defect resolution and successful platform handover.



SUCCESS FACTORS

Chirurgical Budget Adherence

Enforced real-time timesheet tracking to close within €60 of the public funding threshold, avoiding non-compliance.

Iterative Hybrid Framework

Overlapping development and continuous testing cycles enabled early defect detection before final software integration.

Transparent Client Communication

Proactive disclosure of technical and schedule delays preserved trust and fulfilled contractual obligations.

CONTEXT & ADAPTATION

Organizational Context

The company's small size historically favored informal PM processes.

The Vulnerability

Lack of formal risk registers and procurement controls exposed the project to the external supplier's failure.

The Resolution

The team compensated for structural fragility with extreme operational agility and rapid resource reallocation.



Project Improvements

1. Supplier Governance

Embed formal technical acceptance criteria and mandatory quality control gates directly into subcontractor legal agreements.

2. Risk Management

Establish a formal, probability/impact-scored Risk Register right from the project kick-off.

3. Compliance Management

Appoint a dedicated administrative compliance manager from Day 1 to separate financial/TOCC reporting from technical software execution.

4. Financial Contingency

Negotiate and include a risk-based contingency budget (3% to 5%) in all future public tender bids to mitigate zero-margin fragility.



CORE TARGETS FULLY SECURED

The project successfully delivered 100% of the planned technological scope while fully respecting the rigid €57,000 regulatory financial ceiling.

A MANAGERIAL CHALLENGE

Execution analysis demonstrates that the primary threats to the project's critical path were dictated by supplier governance issues, not technical complexity.

HYBRID FRAMEWORK VALIDATION

Combining traditional milestone scheduling with Agile sprints provided the operational agility required to absorb third-party failures.

DURABLE STRATEGIC ASSET

The handover leaves a permanent digital asset that safeguards historical memory, generating long-term cultural and commercial value for Graf S.R.L.

Conclusions

The project succeeded due to the execution resilience of the internal team, not the perfection of the initial plan.



SAPIENZA
UNIVERSITÀ DI ROMA

**THANK YOU
FOR
THE ATTENTION!**
